MATERIAL IN STOCK CHUTE

Platform	4x16' - 4' Above Rail	
Chute	4x18'	
Joists	3x8" - 2' C. Roh Pine	
Deck	2x12" - " " "	
Boards	1½x6" 12" " " "	
Gates	Standard " "	
Posts	6x8" " " Cyp	
Condition of Chute (B)		
Cost to Build " $85.00		Depre. 25% $8.75
Present Value $24.25		

MATERIAL IN PLATFORM

Foundation	12x12" - 8' C. Roh Pine	
Sills	6x8" - 8' " " "	
Joists	3x8" - 3' " " "	
Braces	2x12" - 16' " " "	
Deck	2x12" - Solid " "	
Capty.	500 Bls.	
Condition	(B)	
Cost to Build $505.00		Deprec. 25% $126.25
Present Value $379.75		

MATERIA IN DEPOT

Foundation	12x12" - 8' C. Roh. Pine.	
Sills	6x8" - 12' " " "	
F. Joists	2x10" - 8' " " "	
C "	2x8" - 2' " " "	
Studs	4x6" - At Opng " " 13' Frt. 11' Lom	
Rafters	2x6" - ⅓ Pitch " " — " 20	
Walls.	1x12" — — Siz. " 14+ " 12	
Floor	1x4" — — D.&M. " — " 2 12"	
Ceiling	1x6" — — B.C. " — "	
Doors	3'0" x 7'0" — 18" T	7x7
Windows	10x20" — 12 Lt.	
Roof	Shingled	
Conditin of Building (B)		
Cost " "	$3210.00	Dep. 25%
Present Value	$2407.50	

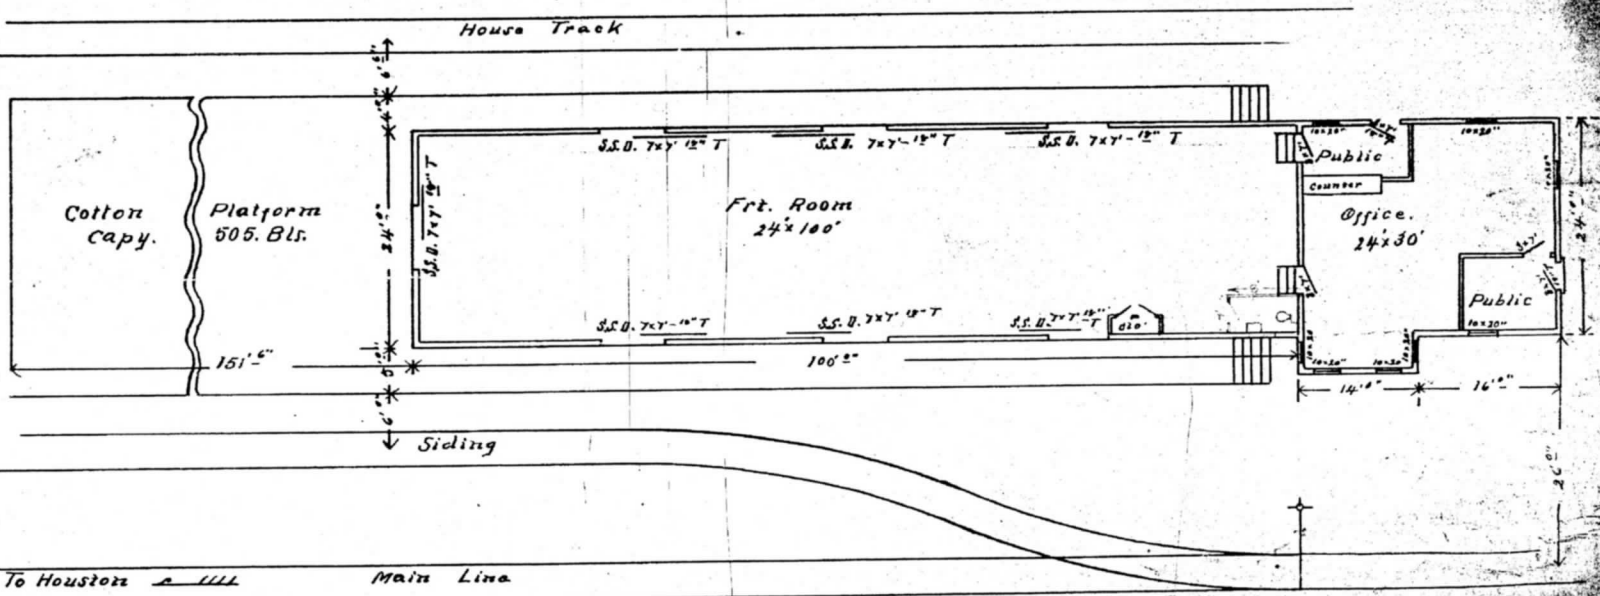



Standard Closet 4x5 ft
Cost to Build $12.00

S.A. & A.P.R.
FREIGHT DEPOT
CUER
STOCK CHUTE
Scale 1in = 10ft
M. of W. Dept.

016 D4

D19 36a
